



Austin - San Antonio
Corridor Council

Welcome to the SH 130 Corridor Summit

Hosted by
Envision Central Texas
and the
Greater Austin-San Antonio Corridor Council

Thanks to our Generous Sponsors:

Barton Springs-Edwards Aquifer

Conservation District

Dwyer Realty

Edelman

Jackson Walker L.L.P.

KLRU-TV

LCRA


Lockwood, Andrews & Newnam

Lone Star Infrastructure

Raba-Kistner Consultants

The Real Estate Council of Austin

Texas Disposal Systems






Transportation Issues

Robert B. Daigh
Texas Department of Transportation

Central Texas Turnpike System

- SH 130
- SH 45 North
- Loop 1
- US 183A
- SH 45 Southeast

**SH 130 (Segments 1 - 4),
SH 45 N, and Loop 1
comprise 2022 Project**

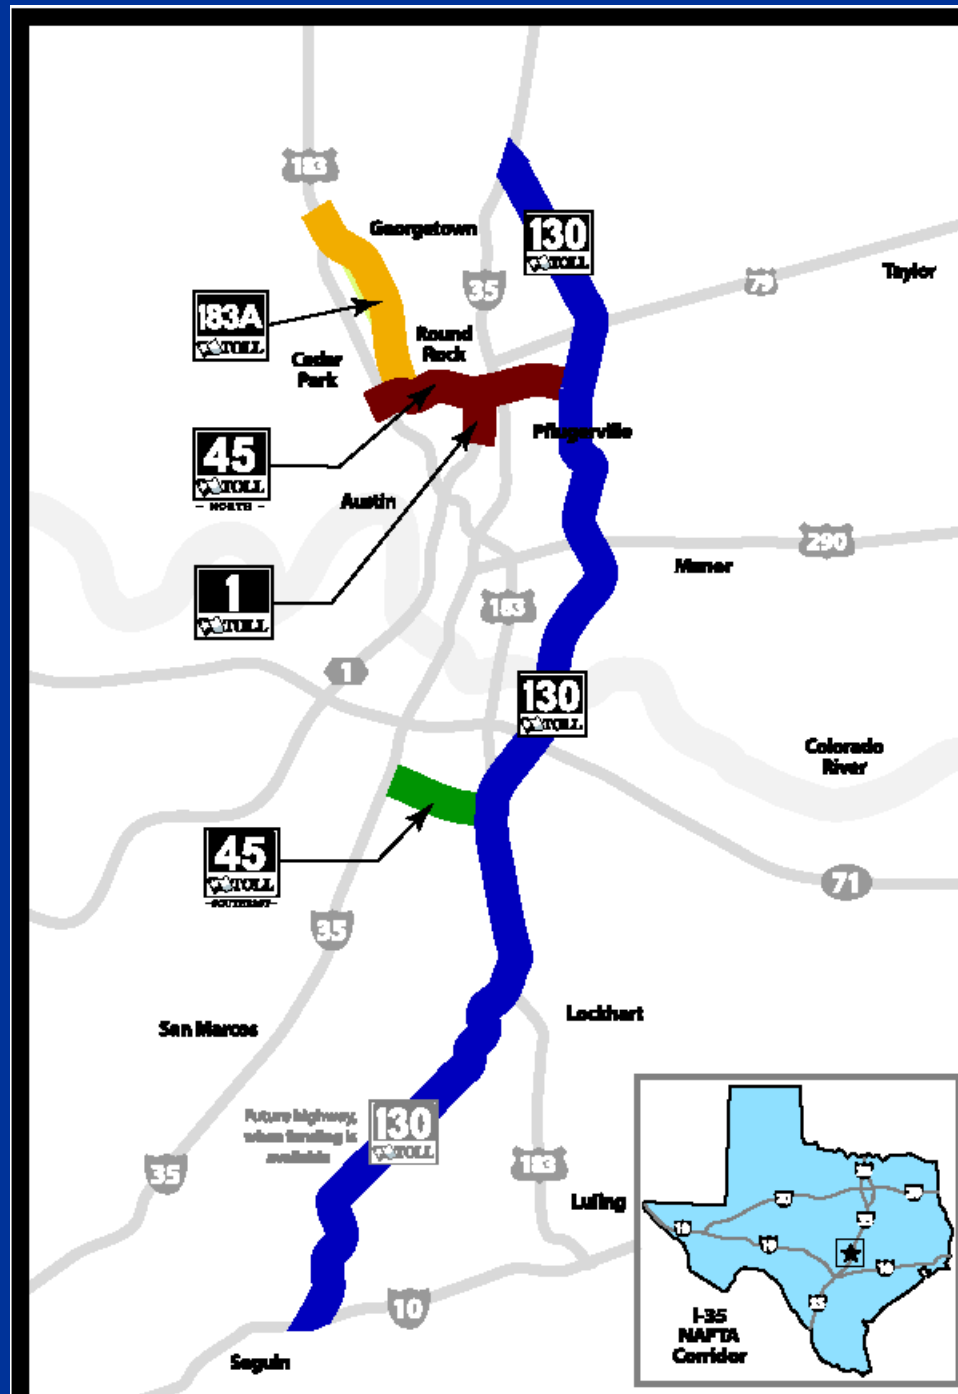

SH 130 Construction Project Status

| | <i>Beginning of Construction</i> | <i>Estimated Completion Dates</i> |
|-----------|--------------------------------------|---|
| Segment 1 | <i>Oct. 2003</i> | <i>Sept. 2007</i> |
| Segment 2 | <i>Dec. 2003</i> | <i>Sept. 2007</i> |
| Segment 3 | <i>Apr. 2004</i> | <i>Sept. 2007</i> |
| Segment 4 | <i>Dec. 2005</i> | <i>Dec. 2007</i> |

Connection with IH 35



San Gabriel Bridge



Segment 2 Structures – Section 5



Working on Bridge 39, 40 sequence along US79. Continued working inside the UPRR ROW for the two SH130 overpass bridges.



SH 130 Segment 2



SH 130 at SH 45N Interchange looking east

Segment 2 Structures – Section 5

SH 45N/SH 130 Interchange Area



Segment 2 Roadway

Continuing with slip form concrete paving south of Cameron and north of Pfluger. Hand pours continuing near plaza area.



SH 130 Segment 2



SH 130 at US 290 looking south

Segment 3 Exc/Emb



SH 130 Segment 3



SH 130 Segment 3



SH 130 at Colorado River
